


August 30, 2019

Project Update - Weeks of September 2 & September 9

Section 1 (see project map)	Section 2 (see project map)	Box Culvert on John Cross Drive
Tuesday, Sept. 3 - Friday, Sept. 6 <ul style="list-style-type: none"> Backfill of Precast Channel Grading Replacing Stream Bed 	Tuesday, Sept. 3 - Friday, Sept. 6 <ul style="list-style-type: none"> Complete Installation of Precast Channel Backfill of Precast Channel Grading Replacing Stream Bed 	Tuesday, Sept. 3 - Friday, Sept. 6 <ul style="list-style-type: none"> Relocate Services on John Cross at Box Culvert location Prepare for Box Culvert Installation
Monday, Sept. 9 - Friday, Sept. 13 <ul style="list-style-type: none"> Backfill of Precast Channel Grading Replacing Stream Bed 	Monday, Sept. 9 - Friday, Sept. 13 <ul style="list-style-type: none"> Backfill of Precast Channel Grading Replacing Stream Bed 	Monday, Sept. 9 - Friday, Sept. 13 <ul style="list-style-type: none"> Install Box Culvert Backfill Box Culvert and Temporary Reinstatement Begin Cast in Place Connections to Precast Channel

Project Timeframe

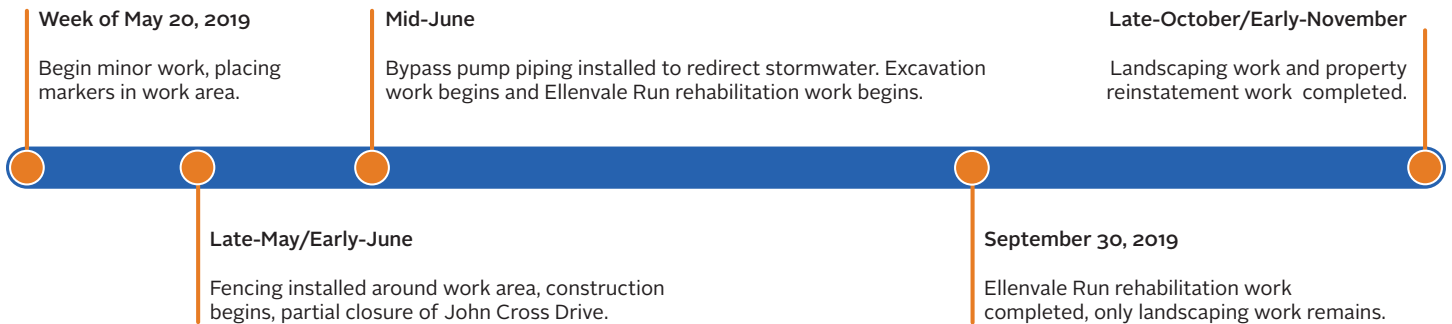

What to Expect

The contractor will have heavy equipment on the roads to facilitate stream reconstruction. Traffic will at times be delayed as temporary traffic control measures may be in place in the areas of work. Work will also be progressing within the channel. Residents can expect to see heavy equipment within the channel removing the existing walls.

During this portion of the project, there will be no pedestrian or vehicle access across the box culvert (shown inside the red box on the attached map) that allows water to flow underneath John Cross Drive.

Project Contacts

Halifax Water
Customer Care Centre
 Mon - Fri 8:00 AM - 8:00 PM
 902-420-9287
 customercare@halifaxwater.ca

Peter Maynard, P.Eng
Project Engineer
Halifax Water
 902-478-7350
 peterma@halifaxwater.ca

Bryan Naugle
President
Brycon Construction
 902-880-2500
 bryan@bryconconstruction.com

Evan Teasdale, P.Eng
Project Engineer
DesignPoint Engineering
 902-832-5597
 evan.teasdale@designpoint.ca

For Project Information & Updates, visit: halifaxwater.ca/project/ellenvale-run-rehabilitation-project-phase-2

**ELLENVALE RUN
PHASE II
DARTMOUTH**

LEGEND

- Channel Rehabilitation
- Road Closure

Meters

0 10 20 40 60 80

Halifax Water

STRAIGHT from the SOURCE

