Community Notice 7

Wanda Lane, Tobin Drive & Ronald Court
Infrastructure Upgrades & Rehabilitation

September 16, 2019

Project Update - Weeks of September 16 & September 23

Wanda Lane

- Excavate/break/install/backfill sanitary and storm mains
- Install sanitary, storm and water services
- Continue asphalt removal up Wanda Lane
- Continue full depth gravel removal and replacement with type 2 gravel
- Continue to install water main
- New storm install from Tobin Drive to Mount Edward
- Start placement of gravels for curb and roadway from Bella Vista Drive to Ronald Court
- Make water line hook up at Ronald Court and start testing

Tobin Drive

- Pressure test water main
- Asphalt/gravel removal
- Type 2 roadway gravel placement
- Placement of type 1 curb and roadway gravels
- Box culvert installation

Ronald Court

- Complete water main to Wanda Lane
- Placement of type 1 curb and roadway gravels
- Test water main

Ellenvale Run

- By-Pass pumping
- Removal of brook infill/ excavation
- Rock mitigation measures
- Rock removal
- Prep bedding for concrete liner
- Liner installation and backfill
- Placement of stone/riffles in liner
- Place bridge abutments
- Prep for and start second cast in place section

Pedestrian Bridge

The bridge pictured on this page will be installed over Ellenvale Run connecting Ronald Court and Kimberley Crescent.

Keep an eye out for future community notices to find out when the new bridge will be installed and when it is open to public use!

Project Contacts

Ian Guppy
Project Manager
Halifax Water
guppyi@halifaxwater.ca
902-476-1610

Jim Cash
Project Manager
Dexter Construction
jimcash@dexter.ca
902-497-7701

Dylan Hayne
Project Manager
Halifax Regional Municipality
hayned@halifax.ca
902-292-3521

Halifax Water
Customer Care Centre
Mon - Fri 8:00 AM - 8:00 PM
customercare@halifaxwater.ca
902-420-9287

For Project Information & Updates, visit: halifaxwater.ca/project/wanda-lane-tobin-drive-ronald-court

STRAIGHT from the SOURCE

WANDA LANE, TOBIN DRIVE & RONALD COURT INFRASTRUCTURE UPGRADES

DARTMOUTH

LEGEND

- New Bridge
- New Paving
- New Sidewalk
- Water Main Renewal
- Old Sanitary Sewer Converted to New Deep Storm Sewer
- New Sanitary Sewer
- Ellenvale Run Channel Upgrades

Meters
0 15 30 60 90 120

N

STRAIGHT from the SOURCE

Halifax Water

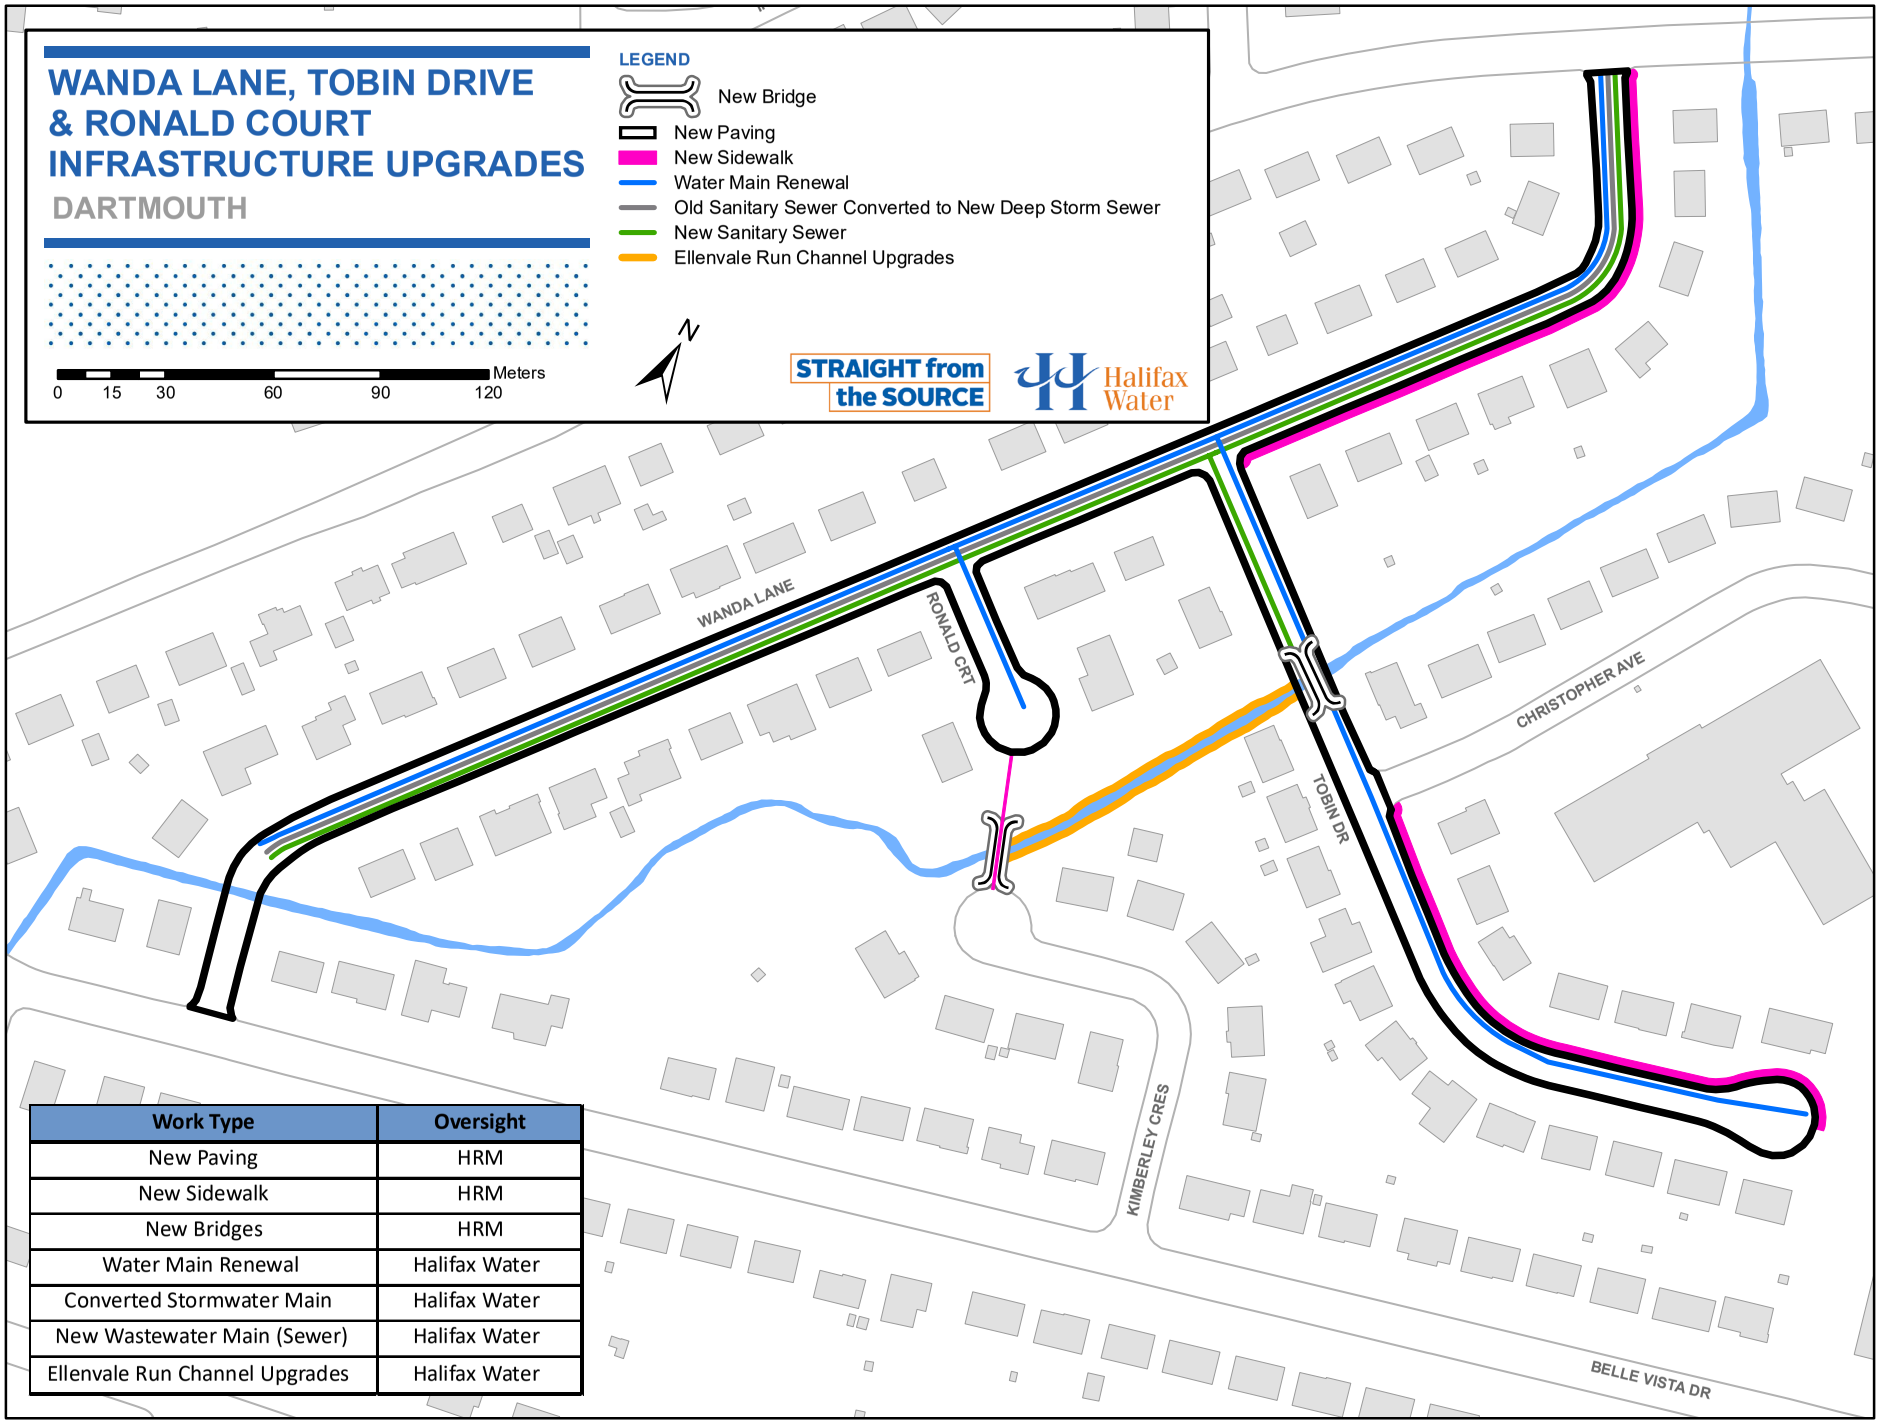

Work Type	Oversight
New Paving	HRM
New Sidewalk	HRM
New Bridges	HRM
Water Main Renewal	Halifax Water
Converted Stormwater Main	Halifax Water
New Wastewater Main (Sewer)	Halifax Water
Ellenvale Run Channel Upgrades	Halifax Water
